
Re-Imagining Update

Hull Elementary



Hull Elementary


- Re-imagine Media Center to foster increased STEM/Collaboration
 - Media & Tech work collaboratively to build 4th-6th
 Enrichment opportunities with STEM and Research
 - Working with CTE to investigate Cyber Security at the elementary level.
- Removing wall between 2 classrooms to build collaborative Spacing for grade levels to work together.

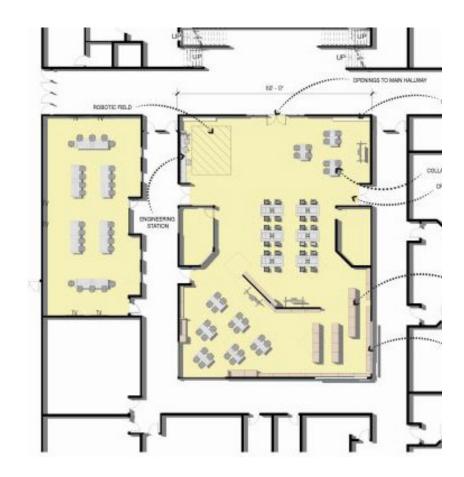



Hull – Media/Tech Center

Hull – Tech Center

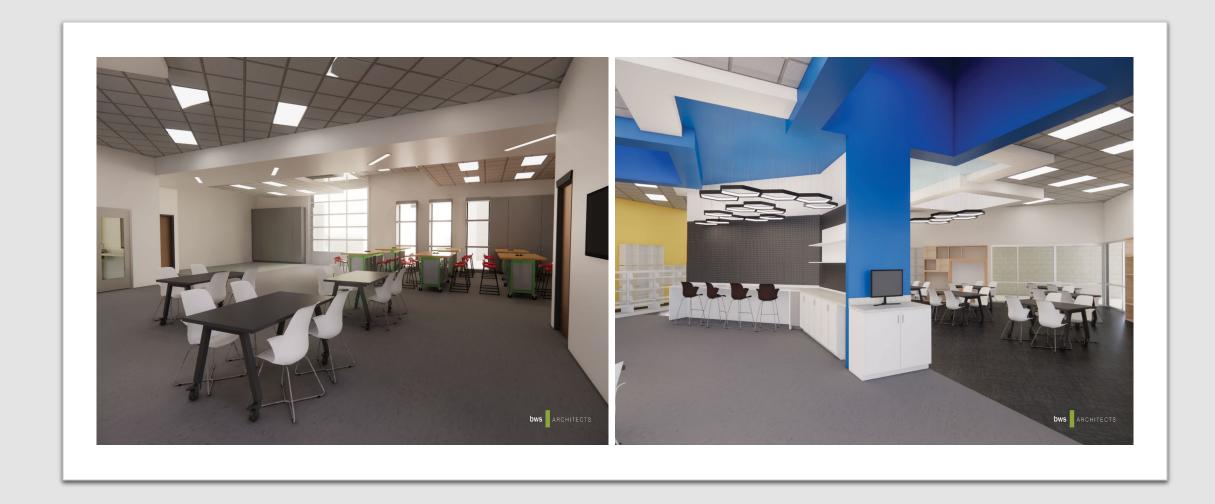



Hull – Tech Center View

Hull - Timeline

Hull Elementary School	DURATION	START DATE	END DATE
Master Plan and Phase I Schematic Design	10 WEEKS	Oct 3, 2023	Nov 29, 2023
Tour of WGA Makerspace		Oct 3, 2023 Actual: 10/9	In-Person Complete
Meeting 1 – Tour of School Review Immediate Needs Develop Program Discuss Future Needs		Oct 4, 2023	In-Person Complete
Meeting 2 –Review Future Space Needs Program, Discuss Initial Concept		Oct 18, 2023 Actual: 10/25	In-Person Complete
Meeting 3 – Review Concepts		Nov 1, 2023 Actual: 11/8	Virtual Complete
Meeting 4 – Review Concepts & Phasing Recommendations		Nov 15, 2023 Actual: 11/29	Virtual Complete
Meeting 5 – Review Finalized Report		Dec 12, 2023 Actual: 12/13	Virtual Complete
CONSTRUCTION DOCUMENTS	6 WEEKS		
Library and Collaboration Phase I – Summer Improvements		Dec 13, 2023 Actual: 1/3/24	Feb 16, 2024
Meeting 6 – Review Interior Items finishes, power, data & furniture		Jan 22, 2024 3:30 pm	In Person with Furniture Vendor
Meeting 7 - Furniture		Feb 7, 2024	
Furniture Order DUE DATE			To Be Confirmed
JOC GMP	4 WEEKS	Feb 16, 2024	Mar 8, 2024
Spring Break	1100000000	Mar 11, 2024	Mar 16, 2024
CONSTRUCTION ADMINISTRATION Concord will provide a detailed schedule	18 WEEKS	TBC	ТВС
Subcontracts, Submittals			
Punch Walk			Jun 25, 2024
Substantial Completion			Jul 2, 2024
Final Completion			Jul 10, 2024
First Day of School			Jul 17, 2024
